

From Production Envelopes to Executable Schedules: Sound Constructive Refinement for High-Mix Manufacturing

Runhao Liu^{1,*†}, Zhengyang Cheng^{2,*}, Fei Ding^{3,*}, Yitong Zhang⁴, Miaolan Zhou¹, Peng Zhang^{5,†}

¹Polytechnic Institute, Zhejiang University, Hangzhou, China
{runhaoliu, 22460342}@zju.edu.cn

²School of Computer Science and Artificial Intelligence, Wuhan University of Technology, Wuhan, China
chzy@whut.edu.cn

³Alibaba Group, Chaoyang District, Beijing, China
dingfei@email.ncu.edu.cn

⁴Computer Science and Technology, Hangzhou City University, Hangzhou, China
32301073@stu.hzcu.edu.cn

⁵School of Mathematical Sciences, Zhejiang University, Hangzhou, China
pengz@zju.edu.cn

*These authors contributed equally. †Corresponding author(s).

Abstract—High-mix manufacturing systems require production plans that are both profitable and refinable into executable machine-level schedules under heterogeneous resources, mold-dependent compatibility, setup losses, delivery windows, and accessory synchronization. We study this problem as a *production-envelope refinement* task. A rolling-horizon mixed-integer linear programming (MILP) planner generates a valid production envelope that fixes daily production, fulfillment, mold states, inventory flows, outsourcing, and unmet-demand variables. A structure-aware constructive scheduler then refines this envelope into concrete order-machine allocations while preserving capacity feasibility, product-mold-machine compatibility, and delivery-window compliance.

The scheduler enforces a one-mold-per-machine-per-day stability rule to avoid intra-day mold fragmentation. We establish residual invariants and prove a soundness theorem: whenever refinement terminates with zero residual fulfillment, the returned allocation is executable with respect to the valid envelope. The framework is implemented as an Advanced Planning and Scheduling (APS) prototype and evaluated on a real industrial case from a Jiangsu smartphone-case manufacturer in China with 37 product types, 150 orders, and over 8.3 million requested units. The proposed stable refinement achieves 100% on-time delivery, eliminates outsourcing, and bounds changeover-driven capacity loss to 1.9–4.6%. Across nine demand and changeover perturbation scenarios, it maintains robust delivery performance, showing that sound envelope refinement is a practical mechanism for reliable manufacturing scheduling.

Index Terms—Terms—Formal Specification, Constructive Refinement, Schedule Synthesis, Production Planning and Scheduling, Cyber-Physical Production Systems, Industrial Case Study

I. INTRODUCTION AND RELATED WORK

High-mix manufacturing systems require production plans that remain executable under interacting discrete constraints. In practice, a plan must simultaneously account for heterogeneous machine capacities, mold-dependent compatibility,

sequence-dependent setup losses, delivery windows, optional outsourcing, and multi-stage synchronization between shell molding and accessory machining. Although modern factories often deploy Enterprise Resource Planning (ERP) or Advanced Planning and Scheduling (APS) systems [1], [2], these systems frequently rely on aggregate or rule-based scheduling logic that hides machine-level conflicts and can produce plans that are profitable in abstraction but non-executable on the shop floor [3], [4]. This mismatch is especially visible in multi-variety, small-batch production, where clustered due dates and frequent mold changes make manual adjustment common despite ongoing digital-transformation efforts [5], [6], [7].

Existing production planning and scheduling methods cover a broad spectrum, including mixed-integer linear programming (MILP) formulations, decomposition-based lot-sizing and scheduling, metaheuristics, and multi-site coordination models [8], [9], [10], [11]. Integrated MILP models can represent capacity, inventory, and order-allocation constraints with high precision [12], [13], [14], [15], but they often rely on abstractions that suppress fine-grained machine-mold compatibility or synchronization details to remain scalable. Dedicated scheduling heuristics and constraint-programming approaches improve shop-floor realism [16], [17], [18], but they are usually evaluated as optimization procedures rather than as refinement mechanisms with explicit consistency guarantees. Data-driven methods such as deep reinforcement learning can learn dispatching policies [19], [20], yet their black-box nature, limited transferability, and deployment cost make it difficult to certify that an aggregate plan has been faithfully realized under plant-specific operational constraints [21], [22], [23].

From a formal-methods perspective, the central difficulty is not only to optimize a production objective, but to guarantee that an abstract plan can be refined into an exe-

cutable machine-level schedule. The planning layer reasons over daily quantities, inventory states, outsourcing decisions, and mold assignments, whereas the scheduling layer must realize these commitments on concrete machines with installed molds and finite effective capacities. This creates an abstraction–refinement problem [24]: a valid production envelope should serve as a formal contract, and the scheduling procedure should synthesize an implementation that preserves this contract. In this paper, we study high-mix manufacturing scheduling as a **production-envelope refinement problem**. A rolling-horizon MILP planner generates a valid envelope satisfying capacity, compatibility, inventory-balance, demand-accounting, and delivery-window constraints. A structure-aware constructive scheduler then refines the envelope into order–machine allocations while enforcing a one-mold-per-machine-per-day stability rule. We establish residual invariants and prove that, whenever the refinement terminates with zero residual fulfillment, the synthesized allocation is executable with respect to the valid production envelope.

Our specific contributions are as follows:

- We formalize high-mix manufacturing scheduling as a **production-envelope refinement problem** that captures heterogeneous capacity, mold exclusivity, product–mold–machine compatibility, delivery windows, outsourcing, unmet demand, setup-induced capacity loss, and accessory synchronization.
- We define a **valid production envelope** as a formal contract between aggregate planning and machine-level synthesis. A rolling-horizon MILP planner generates this envelope, and a **structure-aware constructive refinement** procedure synthesizes executable order–machine allocations from it.
- We prove a **soundness theorem** based on residual invariants: if the constructive scheduler terminates with zero residual fulfillment, the returned allocation preserves planning consistency, capacity feasibility, compatibility, and delivery-window compliance.
- We implement the framework as an **APS prototype** and evaluate it on a real industrial case with 37 product types, 150 orders, and over 8.3 million requested units. Across nominal and nine perturbation scenarios, the stable refinement achieves **100% on-time delivery**, eliminates outsourcing, and bounds changeover loss to **1.9–4.6%**.

II. PRELIMINARIES

We study a production-planning problem arising in discrete manufacturing systems where products require mold-dependent processing on heterogeneous machines. Let $\mathcal{M}$ denote the set of machines and $\mathcal{K}$ the set of molds, where each mold is compatible only with a subset of machines. Production proceeds over a finite horizon $\mathcal{D} = \{1, \dots, H\}$ divided into daily periods, and each machine may operate with at most one mold per day once the mold is installed. Changing a mold incurs substantial setup losses, motivating stable mold assignments across consecutive days.

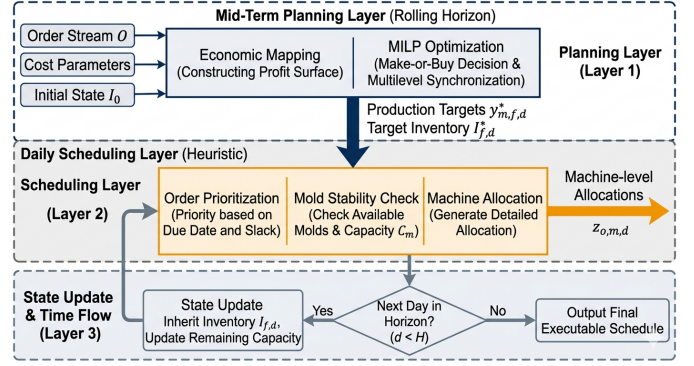


Fig. 1. Overview of proposed method.

Let $\mathcal{F}$ denote the set of products and $\mathcal{O}$ the set of orders. Each order $o \in \mathcal{O}$ specifies a required quantity Q_o and a delivery window $[r_o, \ell_o]$, and partial fulfillment across days is allowed. Products require accessory items whose consumption is proportional to output. Accessory items may be co-produced or sourced from inventory, generating material-balance relations across days.

Economic performance combines in-house revenue, production cost, outsourcing cost, and unmet-demand penalties. We use ρ_o to denote the unit revenue of order o . At an aggregate level, the planning objective can be summarized as

$$\max \left(\sum_{o \in \mathcal{O}} \rho_o (q_o + u_o^{out}) - \sum_{f \in \mathcal{F}} c_f y_f - \sum_{o \in \mathcal{O}} \gamma_o u_o^{out} - \sum_{o \in \mathcal{O}} \pi_o v_o \right), \quad (1)$$

where q_o is the total in-house fulfillment of order o , y_f is the total in-house production envelope of product f , u_o^{out} is the outsourced quantity used to satisfy order o , and v_o is unmet demand.

III. PROPOSED METHOD

A. Overview

The framework consists of two abstraction levels, as shown in Fig. 1. The planning layer solves a rolling-horizon MILP to generate a valid production envelope, fixing production quantities, order fulfillment, mold states, inventory flows, outsourcing, and unmet demand. The scheduling layer constructively refines this envelope into machine-level order allocations under capacity, compatibility, mold stability, and delivery-window constraints. This separation keeps the economic planning problem tractable while making the refinement interface explicit enough to support the soundness argument in Section III-E.

B. Mid-Term Planning Model

Instead of treating production planning as a static constraint satisfaction problem, we formulate the mid-term planning as a profit-driven rolling horizon process. This approach dynamically constructs a decision space where revenue generation is balanced against multi-stage synchronization costs. As outlined in Algorithm 1, the procedure actively identifies

Algorithm 1 Profit-Driven Rolling Horizon Planning.**Input:** Rolling state $(\mathcal{I}_0)$, Order stream $\mathcal{O}$, Cost parameters**Output:** Production envelope $\mathcal{E}^* = (y^*, q^*, x^*, p^*, I^*, u^*, v^*)$

- 1: **State Update:** Inherit accessory inventory $I_{f,0}$ from the previous horizon end-state.
- 2: **Economic Mapping:** Construct the profit surface by mapping unit revenue ρ_o against unmet-demand penalty π_o and outsourcing cost γ_o (Eq. 11).
- 3: **Constraint Injection:**
- 4: Inject machine-mold compatibility and capacity loss constraints.
- 5: Enforce *Multi-Stage Synchronization* to couple shell production $y_{m,f,d}$ with accessory inventory $I_{f,d}$.
- 6: **Optimization:** Solve the Profit-Maximization MILP to determine the optimal "Make-or-Buy" partition $(u_o^*$ vs $q_{o,d}^*)$.
- 7: **Envelope Generation:**
- 8: Extract daily production quotas $y_{m,f,d}^*$ to define the search space for the scheduling layer.
- 9: **return** production envelope $\mathcal{E}^* = (y^*, q^*, x^*, p^*, I^*, u^*, v^*)$.

the optimal Make-or-Buy boundary by evaluating outsourcing trade-offs and rigorously enforcing the coupling between shell molding and accessory production. This ensures that the generated production targets form a theoretically profitable and physically synchronized envelope for the subsequent scheduling layer.

1) *Rolling-Horizon Instantiation:* Let the full planning horizon be $\mathcal{D} = \{1, \dots, H\}$. At each iteration, the planning layer solves the MILP over an active window $\mathcal{D}_{\text{act}} \subseteq \mathcal{D}$ with $|\mathcal{D}_{\text{act}}| \leq W$. To preserve temporal consistency between adjacent windows, boundary states are inherited from fixed decisions made in the previous window:

$$I_{f,d_{\text{start}}-1} = \hat{I}_{f,d_{\text{start}}-1}, \quad x_{m,k,d_{\text{start}}-1} = \hat{x}_{m,k,d_{\text{start}}-1}. \quad (2)$$

Here, d_{start} denotes the first day of the current active window, while $\hat{I}$ and $\hat{x}$ denote inventory and mold states fixed by previously optimized windows.

2) *Decision Variables:* The mid-term planning model uses several groups of decision variables to describe daily production quantities, order fulfillment, material flows, and mold assignments. Table I summarizes their definitions.

3) *Model Constraints:* We first linearize mold changes across consecutive days. Let $\Delta_{m,d} \in \{0, 1\}$ indicate whether machine m changes its installed mold on day d . For $d \geq 2$, $\Delta_{m,d}$ is linked to mold-assignment variation by

$$\Delta_{m,d} \geq x_{m,k,d} - x_{m,k,d-1}, \quad \forall m, k, d, \quad (3)$$

$$\Delta_{m,d} \geq x_{m,k,d-1} - x_{m,k,d}, \quad \forall m, k, d. \quad (4)$$

The effective daily processing-time budget is then defined as

$$C_{m,d}^{\text{eff}} = T_m - \Delta_{m,d} h_m, \quad (5)$$

TABLE I
DECISION VARIABLES IN THE MID-TERM PLANNING MODEL.

Variable	Description
$y_{m,f,d} \geq 0$	Quantity of product f produced on machine m on day d .
$q_{o,d} \geq 0$	Quantity of order o fulfilled by in-house production on day d .
$p_{f,d} \geq 0$	Accessory production for product f on day d .
$I_{f,d} \geq 0$	End-of-day inventory of accessory items for product f .
$u_o \geq 0$	Outsourced quantity for order o .
$v_o \geq 0$	Unmet quantity of order o not satisfied by in-house production or outsourcing.
$x_{m,k,d} \in \{0, 1\}$	Binary indicator: 1 if mold k is installed on machine m on day d .

where T_m denotes the nominal daily available processing time of machine m , and h_m denotes the setup-time loss caused by a mold change. Unit throughputs reported in the case study are derived from this time budget and the processing times $t_{m,f}$. Feasibility is enforced through resource, compatibility, material-flow, and order-timing constraints.

First, regarding machine resources, we enforce daily mold exclusivity and capacity limits. Eq. (6) ensures each machine hosts at most one mold and production fits within the effective processing-time budget:

$$\sum_{k \in \mathcal{K}} x_{m,k,d} \leq 1 \quad \text{and} \quad \sum_f y_{m,f,d} t_{m,f} \leq C_{m,d}^{\text{eff}}, \quad \forall m, d. \quad (6)$$

Additionally, production is permitted only if the installed mold supports the product, enforced by the Big-M constraint: $y_{m,f,d} \leq U_f \sum_k x_{m,k,d} a_{f,k} b_{m,k}$.

Second, regarding material flows, we couple accessory inventory, order fulfillment, and production. For compactness, accessory demand is represented at the product level: when a product requires multiple components, h_f denotes the equivalent requirement after aggregating those components for the corresponding CNC resource. The accessory inventory evolves as

$$I_{f,d} = I_{f,d-1} + p_{f,d} - \sum_{o \in \mathcal{O}_f} q_{o,d} h_f, \quad I_{f,d} \geq 0. \quad (7)$$

Finally, demand accounting, envelope consistency, and delivery-window compliance are enforced by:

$$\sum_{d=r_o}^{\ell_o} q_{o,d} + u_o + v_o = Q_o, \quad \forall o \in \mathcal{O}, \quad (8)$$

$$\sum_{m \in \mathcal{M}} y_{m,f,d} \geq \sum_{o \in \mathcal{O}_f} q_{o,d}, \quad \forall f \in \mathcal{F}, d \in \mathcal{D}. \quad (9)$$

Here $y_{m,f,d}$ is interpreted as a production-envelope quantity that upper-bounds in-house order fulfillment on machine m and day d ; the production-cost term discourages unused internal production.

Order fulfillment is further restricted to the feasible delivery window. Production outside the admissible window is forbidden by

$$q_{o,d} = 0, \quad \forall d < r_o \text{ or } d > \ell_o. \quad (10)$$

Together with the demand-accounting equality in Eq. (8) and the nonnegativity of u_o and v_o , this constraint enforces delivery-window compliance and prevents fulfillment outside the admissible window.

4) *Objective Function*: The mid-term planning objective maximizes economic performance, combining unit revenue, production costs, unmet-demand penalties, and outsourcing costs. The planning objective is:

$$\begin{aligned} \max Z = & \sum_{o \in \mathcal{O}} \rho_o \left(\sum_{d \in \mathcal{D}} q_{o,d} + u_o \right) - \sum_{m \in \mathcal{M}} \sum_{f \in \mathcal{F}} \sum_{d \in \mathcal{D}} c_{f,m} y_{m,f,d} \\ & - \sum_{o \in \mathcal{O}} \gamma_o u_o - \sum_{o \in \mathcal{O}} \pi_o v_o. \end{aligned} \quad (11)$$

The resulting model is solved using a mixed-integer linear programming solver within each rolling window, and the optimized quantities are passed to the scheduling layer as production envelopes.

C. Daily Scheduling Model

Given the production commitments from the mid-term planning layer, the daily scheduling layer assigns the planned quantities $y_{m,f,d}^*$ and $q_{o,d}^*$ to concrete machines. Each assignment must use the mold fixed by the envelope for that machine and day, respect product–mold–machine compatibility, and fit within the remaining effective capacity. The workflow is summarized in Algorithm 2.

For compactness, within a fixed day d , we write $\bar{y}_{m,f}$ for $\bar{y}_{m,f,d}$, and define two residual eligibility predicates:

$$\begin{aligned} \text{Cand}_d(m, f) &\Leftrightarrow \bar{y}_{m,f} > 0 \wedge \bar{C}_m > 0 \\ &\quad \wedge \exists k \in \mathcal{X}_d(m) : a_{f,k} = 1, b_{m,k} = 1, \\ \text{Stable}_d(m, f) &\Leftrightarrow d > 1 \wedge \text{Cand}_d(m, f) \\ &\quad \wedge \exists k \in \mathcal{X}_d(m) \cap \mathcal{X}_{d-1}(m) : \\ &\quad a_{f,k} = 1, b_{m,k} = 1. \end{aligned} \quad (12)$$

To refine the planned quantities, we introduce allocation variables

$$z_{o,m,d} \geq 0, \quad \forall o \in \mathcal{O}, m \in \mathcal{M}, d \in \mathcal{D} \quad (13)$$

where $z_{o,m,d}$ denotes the quantity of order o processed on machine m on day d . These variables disaggregate the planned fulfillment $q_{o,d}^*$ into machine-level assignments. Accordingly, for each order and day, Eq. (14) ensures consistency with the planning-layer decisions.

$$\sum_{m \in \mathcal{M}} z_{o,m,d} = q_{o,d}^*, \quad \forall o, d \quad (14)$$

Similarly, for each product, machine, and day, the aggregated assigned quantities must not exceed the planned production:

$$\sum_{o \in \mathcal{O}_f} z_{o,m,d} \leq y_{m,f,d}^*, \quad \forall f, m, d \quad (15)$$

Algorithm 2 Daily Scheduling Heuristic.

Require: $y_{m,f,d}^*, q_{o,d}^*, x_{m,k,d}^*, t_{m,f}, C_{m,d}^{\text{eff}}$

Ensure: Machine-level allocation z and residual fulfillment $\bar{q}$

```

1:  $z_{o,m,d} \leftarrow 0, \forall o, m, d$ 
2: for each day  $d \in \mathcal{D}$  do
3:    $\mathcal{Q}_d \leftarrow \{o : q_{o,d}^* > 0\}$ , sorted by  $(\ell_o, \ell_o - d, \pi_o)$ 
4:    $\bar{q}_{o,d} \leftarrow q_{o,d}^*, \forall o \in \mathcal{Q}_d$ 
5:   for each machine  $m \in \mathcal{M}$  do
6:      $\mathcal{X}_d(m) \leftarrow \{k : x_{m,k,d}^* = 1\}, \bar{C}_m \leftarrow C_{m,d}^{\text{eff}}$ 
7:      $\bar{y}_{m,f} \leftarrow y_{m,f,d}^*, \forall f \in \mathcal{F}$ 
8:   end for
9:   for each order  $o \in \mathcal{Q}_d$  do
10:    while  $\bar{q}_{o,d} > 0$  do
11:       $f \leftarrow f(o)$ 
12:       $\mathcal{M}_o \leftarrow \{m \in \mathcal{M} : \text{Cand}_d(m, f)\}$ 
13:      if  $\mathcal{M}_o = \emptyset$  then
14:        break
15:      end if
16:       $\mathcal{S}_o \leftarrow \{m \in \mathcal{M}_o : \text{Stable}_d(m, f)\}$ 
17:      Select
18:       $m^* \in \begin{cases} \arg \max_{m \in \mathcal{S}_o} \bar{C}_m, & \mathcal{S}_o \neq \emptyset, \\ \arg \max_{m \in \mathcal{M}_o} \bar{C}_m, & \text{otherwise.} \end{cases}$ 
19:       $u \leftarrow \min\{\bar{q}_{o,d}, \bar{y}_{m^*,f}, \bar{C}_{m^*}/t_{m^*,f}\}$ 
20:       $z_{o,m^*,d} \leftarrow z_{o,m^*,d} + u, \bar{q}_{o,d} \leftarrow \bar{q}_{o,d} - u$ 
21:       $\bar{y}_{m^*,f} \leftarrow \bar{y}_{m^*,f} - u, \bar{C}_{m^*} \leftarrow \bar{C}_{m^*} - u t_{m^*,f}$ 
22:    end while
23:  end for
24: return  $z, \bar{q}$ 
```

Machine capacity feasibility is enforced at the scheduling layer using the same effective capacities $C_{m,d}^{\text{eff}}$ employed by the planning layer. Let $f(o)$ denote the product associated with order o . The total processing time assigned to machine m on day d satisfies Eq. (16), which guarantees that the scheduled workload remains executable given mold changeover losses.

$$\sum_{o \in \mathcal{O}} z_{o,m,d} t_{m,f(o)} \leq C_{m,d}^{\text{eff}}, \quad \forall m, d \quad (16)$$

For any nonzero assignment, the target machine must have an installed compatible mold on that day. Therefore, scheduling must respect product–mold compatibility. Every nonzero assignment satisfies Eq. (17). This ensures that the chosen mold for machine m on day d is capable of producing product $f(o)$.

$$z_{o,m,d} > 0 \Rightarrow \exists k \in \mathcal{K} : x_{m,k,d}^* = 1, a_{f(o),k} = 1, b_{m,k} = 1 \quad (17)$$

Equivalently, we define a derived binary compatibility parameter $\Gamma_{f,m}$, where $\Gamma_{f,m} = 1$ if product f can be processed on machine m under at least one feasible mold configuration. The machine-level compatibility condition can then be written compactly as

$$z_{o,m,d} > 0 \Rightarrow \Gamma_{f(o),m} = 1, \quad (18)$$

where $z_{o,m,d}$ is the assigned quantity of order o on machine m on day d . This compact form is used only for describing plant-level compatibility, while Eq. (17) preserves the explicit product–mold–machine feasibility relation.

To incorporate mold stability and workload balancing considerations, we capture daily mold changes via the binary variation measure:

$$\tilde{\Delta}_{m,d} = \mathbf{1}[\mathcal{X}_d(m) \neq \mathcal{X}_{d-1}(m)], \quad d \geq 2. \quad (19)$$

where $\tilde{\Delta}_{m,d} = 1$ whenever the installed mold state of machine m differs from the preceding day, including mold replacement, installation, or removal. Although mold changes were implicitly penalized in the planning stage through the construction of $C_{m,d}^{\text{eff}}$, the scheduling layer seeks to further reduce unnecessary fluctuations when multiple feasible allocations exist.

In practice, the daily schedule is generated by a lightweight heuristic that orders tasks by due-date urgency, favors mold-continuous assignments to reduce $\tilde{\Delta}_{m,d}$, and adjusts allocations to satisfy the capacity constraint (16) while remaining consistent with the mid-term production plan. This yields an executable per-machine schedule that preserves mold stability and maintains feasible daily workloads across heterogeneous machines.

D. Integrated Planning–Scheduling Framework

The two-layer framework links the mid-term planning model and the daily scheduling model through a structured flow of decision variables. The planning layer first solves the mixed-integer program yielding optimal quantities $y_{m,f,d}^*$, $q_{o,d}^*$, $x_{m,k,d}^*$, $p_{f,d}^*$, $I_{f,d}^*$, u_o^* , and v_o^* .

These variables define the feasible production envelope for each day d , namely $\mathcal{Y}_d = \{(m, f) : y_{m,f,d}^* > 0\}$ and $\mathcal{Q}_d = \{o : q_{o,d}^* > 0\}$, together with the mold configuration $\mathcal{X}_d(m) = \{k : x_{m,k,d}^* = 1\}$. Consistent with the mold-exclusivity constraint in the planning layer, the configuration satisfies

$$|\mathcal{X}_d(m)| \leq 1, \quad \forall m, d. \quad (20)$$

For an active machine with positive planned production, $\sum_f y_{m,f,d}^* > 0$, this set contains exactly one installed mold; for an idle machine, it may be empty. Thus, the framework enforces an at-most-one-mold-per-machine-per-day rule rather than requiring every machine to be occupied in every period.

The scheduling layer refines planning decisions by constructing order–machine allocations $z_{o,m,d}$ satisfying (14) to (16), together with the compatibility implication (17). Thus, the feasible scheduling set for day d is defined as

$$\mathcal{Z}_d = \{z_{o,m,d} \geq 0 : \text{Eqs. (14)–(17) hold}\} \quad (21)$$

and the daily scheduling problem becomes to find $z_{o,m,d} \in \mathcal{Z}_d$ for all $d \in \mathcal{D}$.

Because $y_{m,f,d}^*$, $q_{o,d}^*$, and $x_{m,k,d}^*$ are fixed, the scheduling layer does not modify the planning-layer solution but selects a feasible point $z_{o,m,d}$ consistent with all machine, mold, and capacity restrictions. This hierarchical structure separates multi-period economic optimization from per-period executability

while preserving mathematical consistency between both levels.

E. Soundness of Constructive Refinement

We state the formal guarantee of the constructive refinement layer. The guarantee is conditional: if the scheduler discharges all residual fulfillment requirements, then the synthesized allocation is executable with respect to the valid production envelope.

Let

$$\mathcal{E} = (y^*, q^*, x^*, p^*, I^*, u^*, v^*). \quad (22)$$

be the production envelope generated by the rolling-horizon planner. We call $\mathcal{E}$ valid if it satisfies the rolling-boundary, mold-change, effective-capacity, mold-exclusivity, compatibility, inventory-balance, demand-accounting, production-consistency, and delivery-window constraints in Section III-B. For each day d , it induces the active order set $\mathcal{Q}_d = \{o : q_{o,d}^* > 0\}$ and the installed mold set $\mathcal{X}_d(m) = \{k : x_{m,k,d}^* = 1\}$.

A machine-level allocation $z = \{z_{o,m,d}\}$ is executable if it satisfies planning consistency, production-envelope consistency, capacity feasibility, and compatibility:

$$\begin{aligned} \sum_{m \in \mathcal{M}} z_{o,m,d} &= q_{o,d}^*, & \sum_{o \in \mathcal{O}_f} z_{o,m,d} &\leq y_{m,f,d}^*, \\ \sum_{o \in \mathcal{O}} z_{o,m,d} t_{m,f(o)} &\leq C_{m,d}^{\text{eff}}, & z_{o,m,d} > 0 &\Rightarrow \exists k \in \mathcal{X}_d(m) : a_{f(o),k} = 1, b_{m,k} = 1. \end{aligned} \quad (23)$$

Theorem 1 (Soundness of constructive refinement). *Let $\mathcal{E}$ be a valid production envelope. If Algorithm 2 terminates with $\bar{q}_{o,d} = 0$ for every active order–day pair (o, d) , then the returned allocation z is an executable machine-level schedule with respect to $\mathcal{E}$.*

Proof sketch. Algorithm 2 maintains three residual invariants:

$$\begin{aligned} \bar{q}_{o,d} + \sum_{m \in \mathcal{M}} z_{o,m,d} &= q_{o,d}^*, \\ \bar{y}_{m,f,d} + \sum_{o \in \mathcal{O}_f} z_{o,m,d} &= y_{m,f,d}^*, \\ \bar{C}_m + \sum_{o \in \mathcal{O}} z_{o,m,d} t_{m,f(o)} &= C_{m,d}^{\text{eff}}. \end{aligned} \quad (24)$$

They hold initially because all allocations are zero. The algorithm terminates because each inner iteration either assigns a positive quantity to some machine or exhausts a finite candidate set for the current order–day pair. Each positive assignment adds u to one allocation and subtracts the same amount from the corresponding residual fulfillment, residual production, and residual capacity. Since u is chosen as the minimum of the three available residual quantities, all residual states remain nonnegative. When $\bar{q}_{o,d} = 0$, the first invariant gives planning consistency. Nonnegative residual production and capacity give envelope consistency and capacity feasibility. Finally, the candidate machine set is built from $\mathcal{X}_d(m)$ and the product–mold–machine compatibility relation, so every positive assignment is compatible. Since a valid envelope has $q_{o,d}^* = 0$ outside the delivery window, the refinement also

TABLE II
PRODUCTION RESOURCES IN THE JIANGSU CASE PLANT.

Machine	Qty	Material	Mold type	Throughput (units/day)
GT150	8	Silicone/TPU	GT150; GT130	4,800
GT130	4	TPU	GT130	3,000
CNC (SK750)	2	Metal accessories	Ring/Stand	2,000–4,000

preserves delivery-window compliance. A detailed proof is given in Appendix B.

IV. EXPERIMENTS

A. Refinement Validation Protocol

We evaluate the proposed framework as a *planning-to-scheduling refinement* mechanism rather than as a standalone dispatching heuristic. The goal of the experiments is to check whether different refinement strategies can turn a valid production envelope into executable machine-level schedules while preserving delivery feasibility, capacity constraints, compatibility relations, and multi-stage synchronization.

The evaluation uses a real-world dataset from a Jiangsu smartphone-case manufacturer. Table II summarizes the main resources: GT150 machines provide 4,800 units/day nominal throughput and can operate GT130 molds via adapters; GT130 machines provide 3,000 units/day for thermoplastic polyurethane (TPU) products; computer numerical control (CNC) machines produce ring/stand accessories at 2,000–4,000 units/day. These throughput values are reported for readability; the formal model uses processing-time budgets T_m and unit processing times $t_{m,f}$. Mold changes incur $h_m = 5$ hours of downtime for molding machines.

To isolate how the abstract production envelope is refined into concrete machine-level execution, we instantiate three execution configurations. Scheme C is the constructive refinement procedure covered by Theorem 1; Schemes A and B are diagnostic comparators that expose abstraction and flexibility effects:

- **Scheme A (type-level abstraction):** interprets the envelope only at the aggregate machine-type level, exposing economic plausibility but not individual-machine executability.
- **Scheme B (unrestricted diagnostic execution):** executes the planned workload at machine level while allowing intra-day mold changes. It is used to diagnose the effect of excessive shop-floor flexibility and is not the refinement relation certified by Theorem 1.
- **Scheme C (stable constructive refinement):** refines the envelope at the machine level under the one-mold-per-machine-per-day rule, testing whether stability preserves delivery feasibility.

As additional contract-free baselines, we report two classical dispatching rules: Earliest Due Date (EDD) and Shortest Processing Time (SPT). These rows provide nominal dispatching comparators without the formal consistency guarantee of Scheme C. Unless stated otherwise, nominal results are summarized using On-Time Delivery (OTD), the number of late

TABLE III
NOMINAL-SCENARIO VALIDATION OF REFINEMENT STRATEGIES.

Method	OTD	Late	SyncGap	LoadSigma	COR
A (type)	100.0	0	0.129	0.0775	–
B (machine)	73.3	40	0.224	0.00135	0.0493
C (one-mold)	100.0	0	0.182	0.0161	0.0255
EDD	100.0	0	0.220	0.00212	–
SPT	84.7	23	0.220	0.00474	–

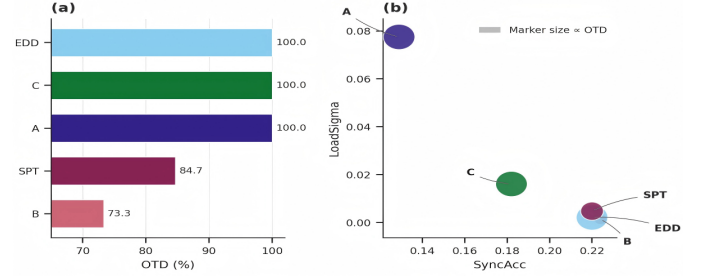


Fig. 2. Nominal-scenario refinement validation dashboard. (a) OTD across refinement strategies and contract-free baselines; (b) SyncGap vs. LoadSigma landscape (marker area $\propto$ OTD).

orders, the diagnostic Synchronization Gap (SyncGap), LoadSigma, and the average Changeover Ratio (COR) on GT130 equipment. Accessory Synchronization Accuracy (SyncAcc) is reported in the planning-contract ablation, where the goal is to measure whether accessory availability covers shell-production demand.

Table III records the nominal scenario, and Figure 2 presents the same comparison in a compact multi-view form.

In addition to SyncAcc, which measures whether accessory availability covers shell-production demand, we report a diagnostic synchronization gap:

$$\text{SyncGap} = \frac{\sum_{d \in \mathcal{D}} |\text{AccProd}_d - \text{AccNeed}_d|}{\sum_{d \in \mathcal{D}} \text{AccNeed}_d}. \quad (25)$$

SyncGap is used as a refinement footprint rather than a feasibility criterion; lower values indicate tighter day-level alignment between accessory production and shell demand.

The nominal scenario validates the role of the certified refinement policy. Scheme A achieves 100% OTD because type-level abstraction hides individual machine conflicts; it shows aggregate plausibility, not machine-level executability. Scheme B exposes a diagnostic failure mode: unrestricted intra-day mold changes fragment execution, causing 40 late orders and reducing OTD to 73.3%. Thus, more shop-floor flexibility does not necessarily yield a more executable implementation.

Scheme C bridges the two levels. The one-mold-per-machine-per-day rule synthesizes stable machine-level allocations while preserving 100% OTD and zero late orders. EDD reaches 100% OTD only in the nominal dispatching comparison, whereas SPT already fails with 23 late orders; neither

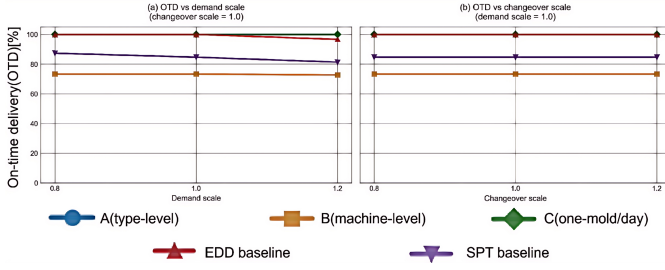


Fig. 3. Robustness of refinement success measured by OTD under varying demand scales (a) and changeover scales (b).

provides the planning-to-scheduling consistency guaranteed by envelope-guided refinement.

B. Robustness of Refinement under Perturbations

A sound refinement procedure should not only succeed under one nominal calibration, but should remain effective when the production envelope is stressed by demand variation and setup-time variation. We therefore scale demand volume and changeover-time coefficients to $\{0.8\times, 1.0\times, 1.2\times\}$, yielding nine perturbation scenarios. These perturbations test whether each refinement policy can continue to discharge the envelope-induced fulfillment requirements under changed load and setup conditions.

Under demand perturbation, Figure 3(a) shows that Scheme C maintains 100% OTD across all stress levels. This indicates that the stability-constrained refinement rule continues to synthesize executable allocations even when the abstract envelope becomes tighter. EDD degrades to approximately 97% at demand scale $1.2\times$, and SPT declines more sharply to 82%, showing that contract-free dispatching is sensitive to demand pressure. Scheme B remains around 73% OTD, confirming that its failure is structural rather than a one-scenario artifact.

Under changeover perturbation, Figure 3(b) shows that Scheme C is insensitive to setup-time inflation in terms of OTD. This is consistent with the intended refinement semantics: because mold changes are concentrated at day boundaries, the one-mold-per-day policy converts setup losses into predictable effective-capacity reductions rather than uncontrolled intra-day fragmentation. Thus, the perturbation study validates Scheme C as a robust refinement policy rather than merely a high-performing nominal scheduler.

C. Refinement Footprint on Machine Utilization

We next quantify how competing schemes reshape workload and idle time across the heterogeneous equipment portfolio.

Machine utilization is reported as a diagnostic footprint rather than an optimization objective. Figure 4 and Table IV show that Scheme B has a small LoadSigma, yet it still leaves 40 orders late because fragmented mold changes create bottleneck congestion. Scheme C has a larger LoadSigma because mold-compatible bottleneck groups absorb more work, while non-critical groups are left partially idle when necessary.

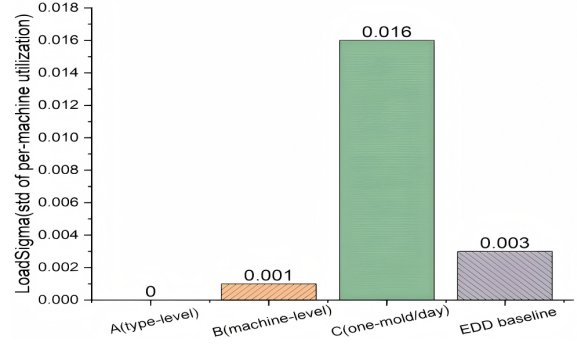


Fig. 4. Average LoadSigma across nine perturbation scenarios. LoadSigma is interpreted as a refinement footprint rather than a standalone objective.

TABLE IV
UTILIZATION AND EXECUTION DESCRIPTORS ACROSS SCHEMES A–C.

Metric	A	B	C
Avg. util. (G1)	95–98%	98–100%	95.7%
Avg. util. (G2)	95–98%	97–100%	98.0%
Avg. util. (G3)	97–98%	70–85%	73.2%
Peak util.	100%	100%	100%
Idle time	Min.	Non-critical groups	Min.
Exec. pattern	Type-level	Fragmented	Stable
Delivery	Abstract feasible	40 late	Zero late

This imbalance is acceptable: under the one-mold-per-day refinement rule, the resulting machine-level allocation remains executable and produces zero late orders.

The Gantt charts in Figure 5 visualize how each configuration realizes the envelope. Scheme A produces smooth group-level patterns because it remains at an abstract machine-type level; these charts therefore hide whether individual machines can actually execute the plan. Scheme B exposes concrete machine assignments, but its frequent intra-day mold reconfigurations fragment execution and lead to deadline violations. Scheme C, in contrast, produces long mold-stable execution intervals, showing that the abstract envelope has been refined into interpretable machine-level blocks.

Figure 6 further confirms that the stability pattern is not a visualization artifact. Across the CNC accessory group (denoted ADPT in the plant data), GT130, and GT150 equipment groups, the machine-level schedules retain unfragmented daily blocks consistent with the one-mold-per-day rule. These diagrams therefore serve as empirical evidence that Scheme C realizes the intended constructive refinement semantics: fixed envelope commitments are mapped to concrete machine assignments without introducing uncontrolled mold-state changes.

D. Stability Cost of Constructive Refinement

We next quantify the cost of enforcing the stable refinement relation. The goal is not to minimize the raw number of mold switches, but to ensure that mold transitions occur in a predictable manner that can be absorbed by the effective-capacity model used in the production envelope.

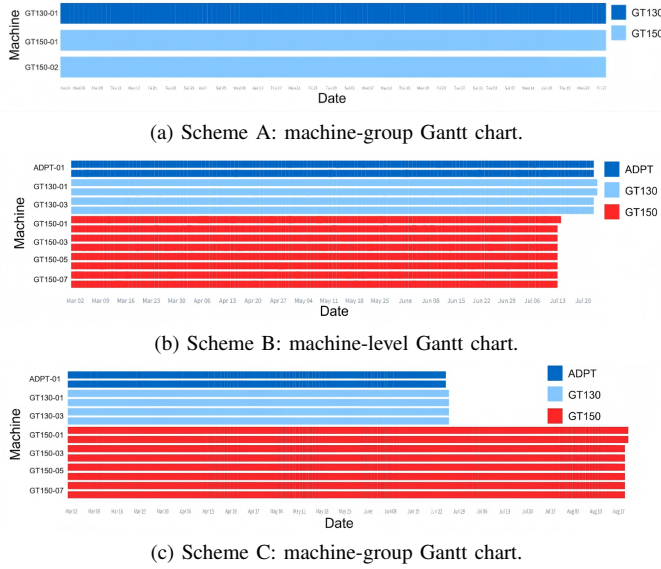


Fig. 5. Refinement realizations under Scheme A, Scheme B, and Scheme C. Scheme A remains abstract, Scheme B permits fragmented machine-level execution, and Scheme C produces mold-stable executable blocks.

TABLE V
CHANGEOVER METRICS FOR MACHINE-LEVEL SCHEDULING SCHEMES.

Metric	Scheme B	Scheme C
Total changeovers (Group 150)	561	763
Avg. per machine (Group 150)	70.1	95.4
Changeover time (Group 150)	140.2 h	190.8 h
Changeover loss (Group 150)	4.1%	4.6%
Total changeovers (Group 130)	156	143
Avg. per machine (Group 130)	39.0	35.8
Changeover loss (Group 130)	2.2%	2.5%
Total changeovers (CNC/ADPT)	77	70
Avg. per machine (CNC/ADPT)	38.5	35.0
Changeover loss (CNC/ADPT)	1.6%	1.9%

Table V and Figure 7 separate two quantities: the number of mold switches and the capacity consumed by those switches. On Group 150, Scheme C increases the number of mold switches from 561 to 763, but the corresponding capacity loss changes only from 4.1% to 4.6%. On GT130 and CNC/ADPT equipment, the losses remain within 1.9–2.5%. Since COR is normalized by the nominal group-specific processing-time budget, the relevant operational cost is the capacity consumed by switching rather than the switch count itself. Thus, the stable refinement policy does not minimize the number of mold switches directly; it bounds their effect on available production capacity.

This distinction is central to the refinement interpretation. Scheme B allows switches to occur inside the day, where they fragment productive intervals and interact poorly with order-level deadlines. Scheme C concentrates mold changes at day boundaries, so the loss is represented as a stable and predictable reduction of daily effective capacity. The experiment therefore validates the design choice behind the refinement rule: stable switch placement is more important

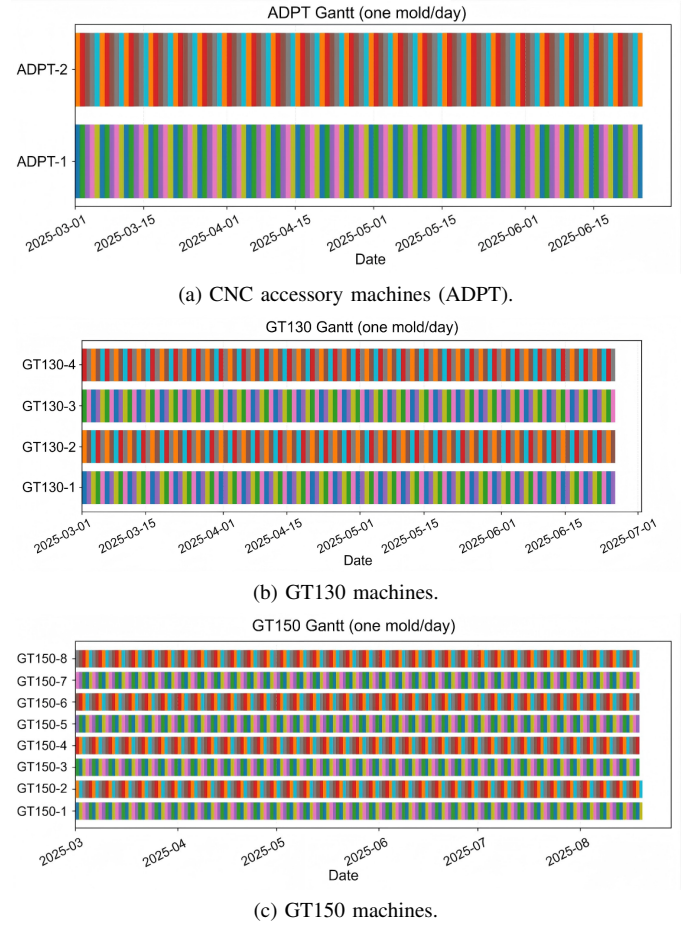


Fig. 6. Detailed machine-level realization of Scheme C across CNC/ADPT, GT130, and GT150 equipment groups. The schedules show stable daily blocks induced by the one-mold-per-day refinement rule.

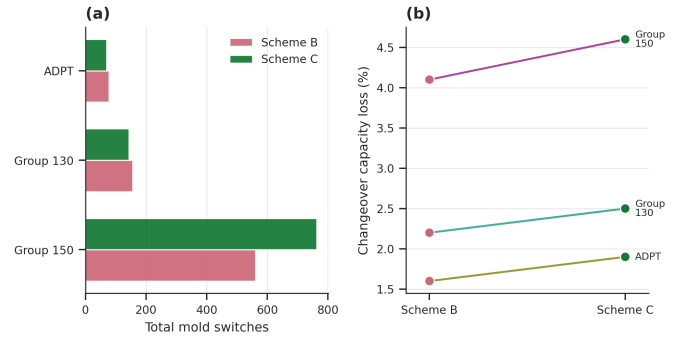


Fig. 7. Stability cost of constructive refinement: (a) total mold switches; (b) induced capacity loss.

for executability than minimizing the absolute number of switches.

E. Ablation: Necessity of the Planning Contract

This ablation directly tests whether the production envelope is necessary for successful refinement. We remove the mid-term planning layer and deploy a stricter no-contract variant,

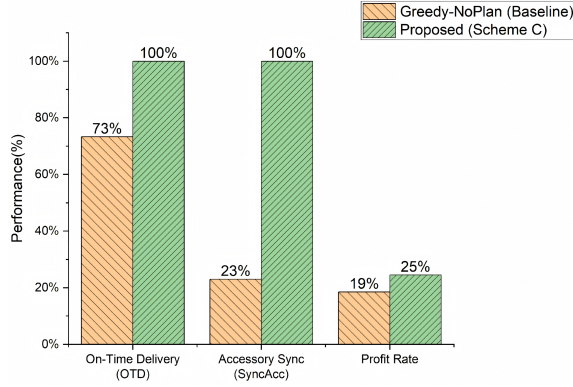


Fig. 8. Ablation of the planning contract. Removing the production envelope causes synchronization collapse and degrades executable refinement.

TABLE VI
COST-RELATED INDICATORS ACROSS SCHEMES A–C.

Metric	A	B	C
Material share	52.8%	47.1%	52.8%
Labor share	47.2%	34.7%	47.2%
Outsourcing share	0%	18.2%	0%
On-time completion	100%	73.3%	100%
Late orders	0	40	0
Outsourced units	0	Significant	0
Execution stability	Medium	Medium	Highest

denoted as *Greedy-NoPlan*, that sequences orders by EDD without MILP-implied production envelopes, inventory states, or look-ahead accessory commitments. Unlike the nominal EDD row in Table III, this ablation disables the planning contract itself and therefore tests both dispatching and multi-stage synchronization without envelope guidance.

Figure 8 shows that removing the planning contract causes SyncAcc to collapse from 1.00 to 0.23, while also degrading delivery performance. This failure explains why the planning layer should be viewed as a contract generator rather than a mere performance enhancement. Without the envelope, the daily scheduler has no formal commitment over future accessory demand, inventory evolution, or bottleneck reservation. It can make locally reasonable assignments, but it cannot preserve the multi-stage shell-accessory synchronization required for executable production. The ablation therefore validates the structural necessity of the production-envelope abstraction.

F. Economic Impact of Executable Refinement

The economic results should also be interpreted through the refinement lens. As shown in Figure 9 and Table VI, Schemes A and C have the same cost composition, with 52.8% material cost, 47.2% labor cost, and no outsourcing. However, Scheme A obtains this result only at the type-level abstraction, whereas Scheme C realizes the same economic outcome as an executable machine-level schedule.

Scheme B demonstrates the economic cost of an unstable refinement policy. Although it operates at the machine level, its fragmented execution leaves 40 orders late and triggers

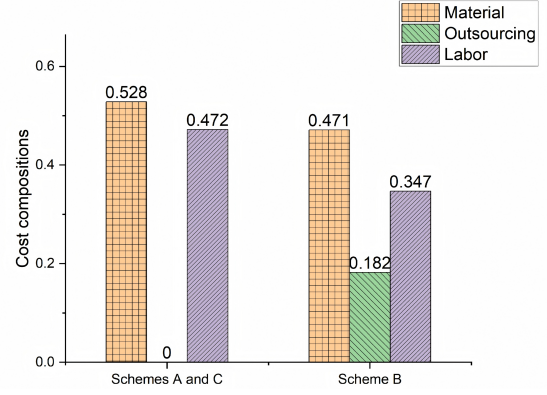


Fig. 9. Economic impact of refinement strategies. Scheme C realizes the same zero-outsourcing cost structure as the abstract type-level plan, but at executable machine-level resolution.

outsourcing, which accounts for 18.2% of total cost. The comparison between Scheme B and Scheme C shows that the economic benefit does not come from adding resources, but from choosing a refinement relation that preserves the feasibility of the production envelope during machine-level synthesis. In this sense, profit improvement is a consequence of executable refinement: once the schedule preserves compatibility, capacity, and stability constraints, expensive outsourcing and delay penalties are avoided.

V. DISCUSSION AND CONCLUSION

This paper formulated high-mix manufacturing scheduling as a production-envelope refinement problem. The planning layer generates a valid envelope that fixes production, inventory, outsourcing, unmet-demand, and mold-state commitments, while the constructive scheduler refines this contract into machine-level allocations. The residual-invariant argument shows that any zero-residual output of the refinement procedure is executable with respect to the envelope, preserving planning consistency, capacity feasibility, compatibility, and delivery-window compliance.

The industrial case study shows that the choice of execution and refinement structure is critical. The diagnostic unrestricted machine-level policy fragments execution and yields only 73.3% OTD, whereas the one-mold-per-machine-per-day constructive refinement rule achieves 100% OTD, eliminates outsourcing, and bounds changeover-driven capacity loss to 1.9–4.6%. The Greedy-NoPlan ablation further shows that removing the planning contract collapses SyncAcc from 1.00 to 0.23, confirming that multi-stage synchronization cannot be recovered by myopic dispatching alone. Future work will extend the framework toward stochastic demand, exact infeasibility certificates for failed refinements, and adaptive stability policies for multi-factory coordination.

REFERENCES

- [1] E. Guzman, B. Andrés, and R. P. Escoto, "Models and algorithms for production planning, scheduling and sequencing problems: A holistic framework and a systematic review," *J. Ind. Inf. Integr.*, vol. 27, p. 100287, 2021.
- [2] D. Rossit, F. Tohmé, and M. Frutos, "A data-driven scheduling approach to smart manufacturing," *J. Ind. Inf. Integr.*, vol. 15, pp. 69–79, 2019.
- [3] A. Moeuf, R. Pellerin, S. Lamouri, S. Tamayo-Giraldo, and R. Barbaray, "The industrial management of smes in the era of industry 4.0," *International Journal of Production Research*, vol. 56, pp. 1118 – 1136, 2018.
- [4] E. Arica and D. Powell, "A framework for ict-enabled real-time production planning and control," *Advances in Manufacturing*, vol. 2, pp. 158 – 164, 2014.
- [5] A. Villalonga, E. Negri, G. Biscardo, F. Castaño, R. Haber, L. Fumagalli, and M. Macchi, "A decision-making framework for dynamic scheduling of cyber-physical production systems based on digital twins," *Annu. Rev. Control.*, vol. 51, pp. 357–373, 2021.
- [6] J. C. Serrano-Ruiz, J. Mula, and R. Poler, "Smart manufacturing scheduling: A literature review," *Journal of Manufacturing Systems*, 2021.
- [7] P. Penchev, P. Vitliemov, and I. Georgiev, "Optimization model for production scheduling taking into account preventive maintenance in an uncertainty-based production system," *Heliyon*, vol. 9, 2023.
- [8] F. Yiğit, M. P. Basilio, M. P. Basilio, and V. Pereira, "A hybrid approach for the multi-criteria-based optimization of sequence-dependent setup-based flow shop scheduling," *Mathematics*, 2024.
- [9] E. Haro, O. Ávalos, J. Gálvez, and O. Camarena, "An integrated process planning and scheduling problem solved from an adaptive multi-objective perspective," *Journal of Manufacturing Systems*, 2024.
- [10] J. Lohmer and R. Lasch, "Production planning and scheduling in multi-factory production networks: a systematic literature review," *International Journal of Production Research*, vol. 59, pp. 2028 – 2054, 2020.
- [11] H. Yuan, Q. Hu, J. Bi, G. Gong, J. Zhang, and M. Zhou, "Machine-level collaborative manufacturing and scheduling for heterogeneous plants," *IEEE Internet of Things Journal*, vol. 11, pp. 16 591–16 603, 2024.
- [12] F. T. Muñoz and J. Ulloa-Navarro, "A make-to-order capacitated lot-sizing model with parallel machines, eligibility constraints, extra shifts, and backorders," *Mathematics*, 2025.
- [13] M. Mohammadi, M. Esmaelian, and A. Atighehchian, "Design of mathematical models for the integration of purchase and production lot-sizing and scheduling problems under demand uncertainty," *Applied Mathematical Modelling*, vol. 84, pp. 1–18, 2020.
- [14] M. Rohaninejad, B. Vahedi-Nouri, Z. Hanzálek, and R. Tavakkoli-Moghaddam, "An integrated lot-sizing and scheduling problem in a reconfigurable manufacturing system under workforce constraints," *International Journal of Production Research*, vol. 62, pp. 3994 – 4013, 2023.
- [15] M. Furlan, B. Almada-Lobo, M. O. Santos, and R. Morabito, "Matheuristic for the lot-sizing and scheduling problem in integrated pulp and paper production," *Comput. Ind. Eng.*, vol. 192, p. 110183, 2024.
- [16] S. Oujana, L. Amodeo, F. Yalaoui, and D. Brodard, "Mixed-integer linear programming, constraint programming and a novel dedicated heuristic for production scheduling in a packaging plant," *Applied Sciences*, 2023.
- [17] D. Popović, N. Bjelić, M. Vidovic, and B. Ratković, "Solving a production lot-sizing and scheduling problem from an enhanced inventory management perspective," *Mathematics*, 2023.
- [18] Çağrı Sel, M. E. Gurkan, and A. Hamzadayı, "Energy-aware production lot-sizing and parallel machine scheduling with the product-specific machining tools and power requirements," *Comput. Ind. Eng.*, vol. 196, p. 110503, 2024.
- [19] W. Song, X. Chen, Q. Li, and Z. Cao, "Flexible job-shop scheduling via graph neural network and deep reinforcement learning," *IEEE Transactions on Industrial Informatics*, vol. 19, pp. 1600–1610, 2023.
- [20] Z. Pan, L. Wang, J. jing Wang, and J. Lu, "Deep reinforcement learning based optimization algorithm for permutation flow-shop scheduling," *IEEE Transactions on Emerging Topics in Computational Intelligence*, vol. 7, pp. 983–994, 2023.
- [21] A. Sunday, U. C. Emeka, E. O. Chukwumuanya, and O. Chikwendu, "Machine learning applications for production scheduling optimization," *Journal of Exploratory Dynamic Problems*, 2025.
- [22] Z. Luo, C. Jiang, L. Liu, X. Zheng, H. Ma, F. Dong, and F. Li, "Deep-reinforcement-learning-based production scheduling in industrial internet of things," *IEEE Internet of Things Journal*, vol. 10, pp. 19 725–19 739, 2023.
- [23] L. Hua, H. Liu, and Y. Pan, "Solving industrial chain job scheduling problems through a deep reinforcement learning method with decay strategy," *Inf. Sci.*, vol. 702, p. 121906, 2025.
- [24] R.-J. Back and J. Wright, *Refinement calculus: a systematic introduction*. Springer Science & Business Media, 2012.

APPENDIX A FORMAL SPECIFICATION SUMMARY

This appendix summarizes the formal objects used by the planning and scheduling layers. The full planning constraints are given in Section III-B; here we only collect the system notation and define the validity of the production envelope used by the refinement proof.

A. System Objects

For readability, this appendix drops calligraphic notation: $M = \mathcal{M}$, $K = \mathcal{K}$, $F = \mathcal{F}$, $O = \mathcal{O}$, and $D = \mathcal{D}$. Let $D = \{1, \dots, H\}$ denote the planning horizon. Each order $o \in O$ has a product type $f(o)$, a quantity Q_o , and a delivery window $[r_o, \ell_o]$. Let

$$O_f = \{o \in O : f(o) = f\}. \quad (\text{A.1})$$

The main parameters are the nominal daily processing-time budget T_m , mold-change loss h_m , unit processing time $t_{m,f}$, product–mold compatibility $a_{f,k}$, machine–mold compatibility $b_{m,k}$, accessory consumption coefficient h_f , unit revenue ρ_o , production cost c_f , outsourcing cost γ_o , and unmet-demand penalty π_o .

The planning layer uses the decision variables

$$y_{m,f,d}, q_{o,d}, p_{f,d}, I_{f,d}, u_o, v_o, x_{m,k,d}, \quad (\text{A.2})$$

where $y_{m,f,d}$ is product-level production-envelope quantity, $q_{o,d}$ is in-house order fulfillment, $p_{f,d}$ and $I_{f,d}$ describe accessory production and inventory, u_o and v_o denote outsourced and unmet quantities, and $x_{m,k,d}$ is the mold-installation indicator.

B. Production Envelope

The optimized planning-layer solution is denoted by

$$\mathcal{E} = (y^*, q^*, x^*, p^*, I^*, u^*, v^*), \quad (\text{A.3})$$

and is called a production envelope. It fixes the aggregate production commitments and mold states that the scheduling layer must refine into machine-level order allocations.

Definition 1 (Valid production envelope). *A production envelope E is valid if it satisfies the rolling-boundary condition in Eq. (2), the mold-change and effective-capacity constraints in Eqs. (3)–(5), the machine-capacity and mold-exclusivity constraints in Eq. (6), the accessory inventory balance in Eq. (7), the demand-accounting and production-consistency constraints in Eqs. (8)–(9), and the delivery-window constraint in Eq. (10). The objective in Eq. (11) selects an economically preferred valid envelope but is not itself a feasibility condition.*

For each day d , a valid envelope induces the active production set, the active order set, and the installed mold set as

$$Y_d = \{(m, f) : y_{m,f,d}^* > 0\}, \quad (\text{A.4})$$

$$Q_d = \{o : q_{o,d}^* > 0\}, \quad (\text{A.5})$$

$$X_d(m) = \{k : x_{m,k,d}^* = 1\}. \quad (\text{A.6})$$

By the mold-exclusivity constraint, every valid envelope satisfies

$$|X_d(m)| \leq 1, \quad \forall m \in M, d \in D. \quad (\text{A.7})$$

For an active machine with positive planned production, this set contains one installed mold; for an idle machine, it may be empty.

APPENDIX B DETAILED PROOF OF THEOREM 1

This appendix provides the detailed proof of the soundness result stated in Section III. The proof expands the residual-invariant argument used by the constructive refinement procedure. Recall that the main theorem is conditional: it proves that a zero-residual output of Algorithm 2 is executable with respect to the valid production envelope, but it does not claim that the greedy refinement is complete.

Let

$$E = (y^*, q^*, x^*, p^*, I^*, u^*, v^*) \quad (\text{B.1})$$

be a valid production envelope generated by the planning layer. For each day d , the constructive scheduler maintains three residual states:

$$\bar{q}_{o,d}, \quad \bar{y}_{m,f,d}, \quad \bar{C}_m, \quad (\text{B.2})$$

where $\bar{q}_{o,d}$ is the remaining fulfillment of order o on day d , $\bar{y}_{m,f,d}$ is the remaining planned production quantity of product f on machine m , and $\bar{C}_m$ is the remaining effective machine capacity.

A. Residual-State Initialization

At the beginning of each day d , Algorithm 2 initializes

$$\bar{q}_{o,d} = q_{o,d}^*, \quad \forall o \in Q_d, \quad (\text{B.3})$$

$$\bar{y}_{m,f,d} = y_{m,f,d}^*, \quad \forall m \in M, f \in F, \quad (\text{B.4})$$

$$\bar{C}_m = C_{m,d}^{\text{eff}}, \quad \forall m \in M. \quad (\text{B.5})$$

All machine-level allocations are initialized as zero:

$$z_{o,m,d} = 0, \quad \forall o, m, d. \quad (\text{B.6})$$

Therefore, before any assignment is made, the following identities hold:

$$\bar{q}_{o,d} + \sum_{m \in M} z_{o,m,d} = q_{o,d}^*, \quad (\text{B.7})$$

$$\bar{y}_{m,f,d} + \sum_{o \in O_f} z_{o,m,d} = y_{m,f,d}^*, \quad (\text{B.8})$$

$$\bar{C}_m + \sum_{o \in O} z_{o,m,d} t_{m,f(o)} = C_{m,d}^{\text{eff}}. \quad (\text{B.9})$$

Moreover, all residual states are nonnegative because the valid production envelope satisfies nonnegativity and effective-capacity constraints.

B. Preservation under One Assignment

Consider one assignment step for order o on day d . Let m^* be the machine selected by Algorithm 2, and let $f(o)$ be the product type of order o . The assigned quantity is

$$u = \min \left(\bar{q}_{o,d}, \bar{y}_{m^*,f(o),d}, \frac{\bar{C}_{m^*}}{t_{m^*,f(o)}} \right). \quad (\text{B.10})$$

The algorithm updates

$$z_{o,m^*,d} \leftarrow z_{o,m^*,d} + u, \quad (\text{B.11})$$

$$\bar{q}_{o,d} \leftarrow \bar{q}_{o,d} - u, \quad (\text{B.12})$$

$$\bar{y}_{m^*,f(o),d} \leftarrow \bar{y}_{m^*,f(o),d} - u, \quad (\text{B.13})$$

$$\bar{C}_{m^*} \leftarrow \bar{C}_{m^*} - u t_{m^*,f(o)}. \quad (\text{B.14})$$

We now verify that the three residual identities are preserved.

First, for the selected order o , the increase of $z_{o,m^*,d}$ by u is exactly matched by the decrease of $\bar{q}_{o,d}$ by u . Hence

$$\bar{q}_{o,d} + \sum_{m \in M} z_{o,m,d} = q_{o,d}^* \quad (\text{B.15})$$

continues to hold. For all other orders, neither their residual fulfillment nor their allocations change, so the identity is unchanged.

Second, for the selected product $f(o)$ on machine m^* , the increase of $z_{o,m^*,d}$ by u is exactly matched by the decrease of $\bar{y}_{m^*,f(o),d}$ by u . Therefore

$$\bar{y}_{m^*,f(o),d} + \sum_{o' \in O_{f(o)}} z_{o',m^*,d} = y_{m^*,f(o),d}^* \quad (\text{B.16})$$

is preserved. For all other machine-product pairs, no corresponding residual production state changes.

Third, for the selected machine m^* , the processing workload increases by $u t_{m^*,f(o)}$, and the residual capacity decreases by exactly the same amount. Thus

$$\bar{C}_{m^*} + \sum_{o' \in O} z_{o',m^*,d} t_{m^*,f(o')} = C_{m^*,d}^{\text{eff}} \quad (\text{B.17})$$

continues to hold. For all other machines, neither workload nor residual capacity changes.

Finally, since u is upper-bounded by $\bar{q}_{o,d}$, $\bar{y}_{m^*,f(o),d}$, and $\bar{C}_{m^*}/t_{m^*,f(o)}$, the updated residual states remain nonnegative:

$$\bar{q}_{o,d} \geq 0, \quad \bar{y}_{m^*,f(o),d} \geq 0, \quad \bar{C}_{m^*} \geq 0. \quad (\text{B.18})$$

Therefore, by induction over all assignment steps, the residual identities and nonnegativity conditions hold throughout Algorithm 2.

C. Deriving Executability from Zero Residuals

Assume that Algorithm 2 terminates with

$$\bar{q}_{o,d} = 0, \quad \forall o \in Q_d, \quad d \in D. \quad (\text{B.19})$$

Using identity (B.7), we obtain

$$\sum_{m \in M} z_{o,m,d} = q_{o,d}^*, \quad \forall o, d, \quad (\text{B.20})$$

which proves planning consistency.

Since all residual production quantities remain nonnegative, identity (B.8) implies

$$\sum_{o \in O_f} z_{o,m,d} \leq y_{m,f,d}^*, \quad \forall f, m, d. \quad (\text{B.21})$$

Thus the machine-level allocation never exceeds the production quantities fixed by the valid envelope.

Similarly, since all residual capacities remain nonnegative, identity (B.9) implies

$$\sum_{o \in O} z_{o,m,d} t_{m,f(o)} \leq C_{m,d}^{\text{eff}}, \quad \forall m, d. \quad (\text{B.22})$$

Therefore, every machine respects its effective capacity after setup losses.

It remains to show compatibility. Algorithm 2 constructs the candidate machine set using the mold state fixed by the envelope and the product-mold-machine compatibility relation. Hence a positive assignment can only be made when there exists an installed mold $k \in X_d(m)$ such that

$$a_{f(o),k} = 1, \quad b_{m,k} = 1. \quad (\text{B.23})$$

Therefore,

$$z_{o,m,d} > 0 \Rightarrow \exists k \in X_d(m) : a_{f(o),k} = 1, \quad b_{m,k} = 1, \quad (\text{B.24})$$

which proves product-mold-machine compatibility.

Finally, because the valid production envelope enforces

$$q_{o,d}^* = 0, \quad \forall d < r_o \text{ or } d > \ell_o, \quad (\text{B.25})$$

planning consistency gives

$$\sum_{m \in M} z_{o,m,d} = 0, \quad \forall d < r_o \text{ or } d > \ell_o. \quad (\text{B.26})$$

Thus the refined machine-level schedule does not assign production outside the admissible delivery window.

Combining planning consistency, production-envelope consistency, capacity feasibility, compatibility, and delivery-window preservation proves that the returned allocation is an executable machine-level schedule with respect to the valid production envelope.

D. Scope of the Guarantee

The result above is a soundness guarantee. It states that if Algorithm 2 returns a zero-residual allocation, then the returned schedule is executable. It is not a completeness guarantee. If the constructive scheduler leaves nonzero residual fulfillment, this only shows that the particular greedy refinement rule failed to construct a complete allocation; it does not prove that no feasible allocation exists. Proving infeasibility would require an exact MILP, CP, SMT, or SAT-style encoding of the daily refinement problem.

APPENDIX C

INDUSTRIAL CASE DETAILS

This appendix records instance-level details that are not fully expanded in the main text. The production resources are already reported in Table II and are not repeated here.

A. Instance Scale and Demand Structure

The industrial instance comes from a smartphone protective-case manufacturer in Jiangsu Province, China. It contains 37 product types and 150 customer orders over an eight-month horizon, with a total requested quantity exceeding 8.3×10^6 units. Monthly demand is highly uneven, ranging from approximately 0.6M to 1.5M units, which creates clustered deadline pressure and short-term bottleneck risk.

Each product is associated with a mold type and a material type. Some products additionally require accessory components, such as heat-dissipation rings or stands. Each order o specifies a product type $f(o)$, quantity Q_o , and admissible processing interval $[s_o, d_o]$. In the formal model, this interval is represented as the delivery window $[r_o, \ell_o]$.

B. Compatibility and Synchronization Constraints

Mold-machine compatibility is represented by $b_{m,k}$, and product-mold compatibility is represented by $a_{f,k}$. A compact plant-level compatibility indicator can be derived as

$$\Gamma_{f,m} = \mathbf{1}[\exists k \in K : a_{f,k} = 1, b_{m,k} = 1]. \quad (\text{C.1})$$

The main model uses the stronger explicit condition that a nonzero machine-level allocation must use a mold actually installed on that machine and day:

$$z_{o,m,d} > 0 \Rightarrow \exists k \in K : x_{m,k,d}^* = 1, a_{f(o),k} = 1, b_{m,k} = 1. \quad (\text{C.2})$$

Accessory synchronization is required whenever a product needs a ring or stand. In the raw plant description, accessory availability must satisfy

$$q_{o,t}^{\text{acc}} \geq x_{o,m,t}, \quad (\text{C.3})$$

where $x_{o,m,t}$ is the shell quantity assigned to machine m at time t . In the planning formulation, this is represented through the inventory-balance constraint and nonnegative end-of-day inventory. This allows accessories to be prepared before future shell demand while preventing infeasible shell-production commitments.

C. Operational Assumptions

Raw materials follow a fixed three-day procurement lead time, and all initial inventories are set to zero. The plant operates under three shifts:

$$0:00-8:00, \quad 8:00-16:00, \quad 16:00-24:00. \quad (\text{C.4})$$

Each active machine requires one operator per shift, and piece-rate wages are $\{0.10, 0.12, 0.15\}$ CNY per unit.

Mold changes introduce a fixed setup loss:

$$\tau_m(k, k') = \begin{cases} h_m, & k \neq k', \\ 0, & k = k'. \end{cases} \quad (\text{C.5})$$

The planning layer converts this loss into effective processing-time capacity through $C_{m,d}^{\text{eff}} = T_m - \Delta_{m,d} h_m$, while the scheduling layer refines the fixed mold configuration without introducing additional mold states.

D. Case Characteristics

The case plant combines heterogeneous machine capacities, limited mold-machine compatibility, adapter-based execution of GT130 molds on GT150 machines, clustered deadlines, multi-stage shell-accessory synchronization, three-day material lead times, shift-dependent labor costs, sequence-dependent mold-change losses, and optional outsourcing. These coupled constraints explain why aggregate planning alone may be non-executable and why myopic daily dispatching cannot reliably prepare future accessories or reserve bottleneck capacity.

APPENDIX D METRIC DEFINITIONS

This appendix defines the evaluation metrics used in the case study. The goal is to avoid ambiguity between delivery, synchronization, load-balance, changeover, and economic metrics.

Let O be the set of customer orders and let C_o denote the completion day of order o . The latest admissible delivery day is ℓ_o . Let M be the machine set, D the planning horizon, and $\mathcal{G}$ the set of equipment groups.

A. On-Time Delivery

On-Time Delivery (OTD) measures the fraction of orders completed within their delivery windows:

$$\text{OTD} = \frac{\sum_{o \in O} \mathbf{1}[C_o \leq \ell_o]}{|O|}. \quad (\text{D.1})$$

When reported as a percentage, Eq. (D.1) is multiplied by 100.

B. Number of late orders

The number of late orders is

$$\text{LateOrders} = \sum_{o \in O} \mathbf{1}[C_o > \ell_o]. \quad (\text{D.2})$$

C. Mean lateness

The lateness of order o is

$$L_o = \max(0, C_o - \ell_o), \quad (\text{D.3})$$

and the mean lateness is

$$\text{MeanLate} = \frac{1}{|O|} \sum_{o \in O} L_o. \quad (\text{D.4})$$

D. Machine utilization

Let $W_{m,d}$ denote the productive workload assigned to machine m on day d , and let $C_{m,d}^{\text{eff}}$ be the effective available capacity after setup losses. The utilization of machine m over the horizon is

$$\text{Util}_m = \frac{\sum_{d \in D} W_{m,d}}{\sum_{d \in D} C_{m,d}^{\text{eff}}}. \quad (\text{D.5})$$

The group-level utilization reported in the paper is the average of Util_m over machines belonging to the same equipment group.

E. Load variance

Let $\mathcal{G}$ denote the set of equipment groups and let Util_g be the average utilization of group g . The load-balance statistic is computed as the standard deviation of group-level utilizations:

$$\text{LoadSigma} = \sqrt{\frac{1}{|\mathcal{G}|} \sum_{g \in \mathcal{G}} (\text{Util}_g - \overline{\text{Util}})^2}, \quad (\text{D.6})$$

where

$$\overline{\text{Util}} = \frac{1}{|\mathcal{G}|} \sum_{g \in \mathcal{G}} \text{Util}_g. \quad (\text{D.7})$$

Lower LoadSigma indicates more balanced group-level workload. However, load balance should not be interpreted independently of OTD, because a low variance may still correspond to infeasible or late execution.

F. Changeover Ratio

Let $S_{m,d}$ be the setup or mold-change time loss of machine m on day d , and let T_m be the nominal daily processing-time budget of machine m . The Changeover Ratio (COR) is

$$\text{COR} = \frac{\sum_{m \in M} \sum_{d \in D} S_{m,d}}{\sum_{m \in M} \sum_{d \in D} T_m}. \quad (\text{D.8})$$

When reported for a specific equipment group $G \subseteq M$, the sums in Eq. (D.8) are restricted to machines $m \in G$.

G. Accessory Synchronization

Accessory Synchronization Accuracy (SyncAcc) measures whether accessory availability covers the accessory demand induced by shell production:

$$\text{SyncAcc} = \frac{\sum_{d \in D} \min(\text{AccAvail}_d, \text{AccNeed}_d)}{\sum_{d \in D} \text{AccNeed}_d}. \quad (\text{D.9})$$

Here, AccNeed_d is the accessory quantity required by shell production on day d , and AccAvail_d is the accessory quantity available for use on day d , including inventory carried from previous days and same-day accessory production. A value of $\text{SyncAcc} = 1$ indicates that accessory availability fully covers shell-production demand, while lower values indicate synchronization shortages.

H. Accessory Synchronization Gap

We also report a diagnostic synchronization gap:

$$\text{SyncGap} = \frac{\sum_{d \in \mathcal{D}} |\text{AccProd}_d - \text{AccNeed}_d|}{\sum_{d \in \mathcal{D}} \text{AccNeed}_d}. \quad (\text{D.10})$$

Unlike SyncAcc, SyncGap is not a feasibility metric. It measures the day-level mismatch between accessory production and shell-production demand. A schedule may have $\text{SyncAcc} = 1$ while retaining a nonzero SyncGap if accessories are pre-built and carried through inventory.

I. Economic cost shares

Let MatCost, LaborCost, OutCost, and DelayCost denote material, labor, outsourcing, and delay-penalty costs, respectively. The total cost is

$$\text{TotalCost} = \text{MatCost} + \text{LaborCost} + \text{OutCost} + \text{DelayCost}. \quad (\text{D.11})$$

The cost share of component r is

$$\text{Share}_r = \frac{\text{Cost}_r}{\text{TotalCost}}. \quad (\text{D.12})$$

J. Profit rate

Let Revenue denote total realized revenue. Profit rate is defined as

$$\text{ProfitRate} = \frac{\text{Revenue} - \text{MatCost} - \text{LaborCost}}{\text{Revenue} - \frac{\text{OutCost} + \text{DelayCost}}{\text{Revenue}}}. \quad (\text{D.13})$$
